



**LATA Environmental Services
of Kentucky, LLC**

761 Veterans Avenue
Kevil, KY 42053

February 7, 2013

Deliverable No: 170

PAD-SO-13-2857

bj FEB 7 3:37PM

Mr. Reinhard Knerr, Paducah Site Lead
Portsmouth/Paducah Project Office
U.S. Department of Energy
P.O. Box 1410
Paducah, Kentucky 42002-1410

Dear Mr. Knerr:

DE-AC30-10CC40020: Deliverable No. 170—*Uranium Enrichment Toxic Substances Control Act Federal Facilities Compliance Agreement Quarterly Progress Report for the Paducah Gaseous Diffusion Plant, Paducah, Kentucky, October 1 through December 31, 2012, PAD-SO-0044/V4*

Enclosed is the *Uranium Enrichment Toxic Substances Control Act Federal Facilities Compliance Agreement Quarterly Progress Report for the Paducah Gaseous Diffusion Plant, Paducah, Kentucky, October 1 through December 31, 2012, PAD-SO-0044/V4* (UE TSCA FFCA).

This final UE TSCA FFCA Quarterly Progress Report is a shelf document that is required to be available for U.S. Environmental Protection Agency inspection. The information within this report will be included in the 2012 UE TSCA FFCA Annual Compliance Report.

If you have any questions, please contact Ed King at (270) 441-5152

Sincerely,

LATA Environmental Services of Kentucky, LLC

Mark J. Doff
Paducah Project Manager

Enclosure

cc:

DMC, Kevil

e-copy:

kim.crenshaw@lex.doe.gov

rachel.blumenfeld@lex.doe.gov

reinhard.knerr@lex.doe.gov

rob.seifert@lex.doe.gov

william.creech@lex.doe.gov

**Uranium Enrichment
Toxic Substances Control Act
Federal Facilities Compliance Agreement
Quarterly Progress Report for the
Paducah Gaseous Diffusion Plant, Paducah, Kentucky
October 1 through December 31, 2012**



This document is approved for public release per review by:

Merlin Shuman
LATA Kentucky Classification Support

2-6-2013
Date

**Uranium Enrichment
Toxic Substances Control Act
Federal Facilities Compliance Agreement
Quarterly Progress Report for the
Paducah Gaseous Diffusion Plant, Paducah, Kentucky
October 1 through December 31, 2012**

Date Issued—February 2013

Prepared for the
U.S. DEPARTMENT OF ENERGY
Office of Environmental Management

LATA ENVIRONMENTAL SERVICES OF KENTUCKY, LLC
managing the
Environmental Remediation Activities at the
Paducah Gaseous Diffusion Plant
under contract DE-AC30-10CC40020

CONTENTS

TABLES	iii
FIGURE	iii
ACRONYMS	iv
1. INTRODUCTION.....	1
2. INTERIM MEASURES	1
2.1 AIR SAMPLING.....	1
2.1.1 Requirements	1
2.1.2 Work Completion Date.....	1
2.1.3 Activity for this Quarter	2
3. COMPLIANCE MEASURES.....	3
3.1 PROCESS LUBRICATION OIL REMOVAL	3
3.2 SPILL CLEANUP	3
3.2.1 Requirements	3
3.2.2 Work Completion Date.....	3
3.2.3 Activity for this Quarter	3
3.3 ELECTRICAL CABLES AND ASSOCIATED EQUIPMENT	5
3.3.1 Requirements	5
3.3.2 Work Completion Date.....	5
3.3.3 Activity for this Quarter	5
3.4 DISPOSAL	5
3.4.1 Requirements	5
3.4.2 Work Completion Date.....	5
3.4.3 Activity for this Quarter	6

TABLES

1. Fourth Quarter CY 2012 TSCA FFCA Air Sampling Results	2
2. PCB Waste Shipped Off-Site Disposal Activities: Waste Shipped Off-Site and Certificates of Disposal Received October 1 through December 31, 2012.....	7

FIGURE

1. Quarterly Summary of PCB Gasket Spills	4
---	---

ACRONYMS

BEJ	best engineering judgment
<i>CFR</i>	<i>Code of Federal Regulations</i>
CY	calendar year
DOE	U.S. Department of Energy
EPA	U.S. Environmental Protection Agency
FFCA	Federal Facilities Compliance Agreement
NESHAP	National Emission Standard for Hazardous Air Pollutants
PCB	polychlorinated biphenyl
RCRA	Resource Conservation and Recovery Act
TSCA	Toxic Substances Control Act
UE	uranium enrichment

1. INTRODUCTION

The Uranium Enrichment (UE) Toxic Substances Control Act (TSCA) Federal Facilities Compliance Agreement (FFCA) signed by U.S. Department of Energy (DOE) and the U.S. Environmental Protection Agency (EPA) on February 20, 1992, and modified in 1997, requires quarterly reports that summarize progress toward completing polychlorinated biphenyl (PCB)-related compliance measures. These measures include troughing, air sampling, process lubrication oil removal, spill cleanup, and disposal. The quarterly reports will be maintained at the DOE Site Office and available to EPA, upon request, 45 days following the end of the quarter. The quarterly reports are required to be included in DOE's Annual Compliance Agreement Report. The following summaries satisfy the UE TSCA FFCA quarterly reporting requirements for October 1 through December 31, 2012.

2. INTERIM MEASURES

2.1 AIR SAMPLING

2.1.1 Requirements

Attachment I, Section 1 (D), of the UE TSCA FFCA states the following:

Air Sampling – Consistent with DOE's monitoring at the facilities, PCB air sampling will be continued in process buildings with motor exhaust systems. At least 5 samples will be taken per process building per year. For each of these buildings, samples will be taken quarterly every calendar year, at least 30 days apart, with an additional set of samples taken sometime during the year. For each periodic (annual) air monitoring activity in a building, there are two kinds of sampling sites: best engineering judgment (BEJ) selected sites and randomly selected sites. The same BEJ sites may be selected for more than one monitoring period. The randomly selected sites shall be different from the BEJ sites and shall be newly selected for each periodic monitoring activity according to the attached guidance provided in the appended "Selection of Random Sampling Sites." It would be a rare coincidence for the same randomly selected location in the same building to be sampled in more than one periodic monitoring activity. DOE shall report quarterly to the EPA any PCB concentrations greater than 0.5 micrograms per cubic meter measured from any air-monitoring sampler at any location. Upon receipt of any such measurement data, EPA will contact DOE to address further monitoring requirements and any other required actions. Should EPA conclude that air sampling results produced pursuant to this Agreement so warrant, EPA and DOE shall meet and shall agree upon additional protective measures to be taken by DOE.

2.1.2 Work Completion Date

Work must be complete one year after facility shutdown.

2.1.3 Activity for this Quarter

The UE TSCA FFCA requires that PCB air sampling be conducted in process buildings with motor exhaust duct ventilation systems. These buildings include the C-331, C-333, C-335, and C-337 process buildings at the Paducah facility. At least five samples are required to be taken per building per year; at least one of the five samples will be taken at a BEJ selected site, with the remainder of the sites to be selected randomly. For each of the buildings, the samples must be taken quarterly every calendar year (CY), at least 30 days apart. DOE is required to report quarterly to EPA any PCB concentrations greater than 0.5 µg/m³ measured from any air-monitoring sampler at any location.

Air samples for the fourth quarter were collected November 1, 2012. The results of all the samples collected for the fourth quarter of CY 2012 are shown in Table 1. The quarterly sample sets were obtained more than 30 days apart, as required. The sampling was conducted as described in National Institute for Occupational Safety and Health 5503. The volumes and flow rates, as noted, were necessary to achieve the detection limit required by the UE TSCA FFCA. All samples were less than detection limit reported by the laboratory. These nondetections confirm the sample results did not exceed the UE TSCA FFCA reporting level of 0.5 µg/m³.

Table 1. Fourth Quarter CY 2012 TSCA FFCA Air Sampling Results

Sample Numbers	Sample Date	Building	Floor	Sample Coordinates	Method of Selection	Results* (µg/m ³)	Pump Flow Rate (liters/minute)	Air Volume Sampled (liters)
PCB13-AIR-01-01	11/01/12	C-331	CELL	62, 55 NE of Y-19	Random	PCBs not detected above laboratory reporting limits	1.11	561
PCB13-AIR-01-02	11/01/12	C-333	CELL	9, 76 N of Ca-24	Random	PCBs not detected above laboratory reporting limits	1.17	590
PCB13-AIR-01-03	11/01/12	C-335	GROUND	78, 0 At DD-1	Random	PCBs not detected above laboratory reporting limits	1.14	574
PCB13-AIR-01-04	11/01/12	C-337	CELL	77, 110 SE of Na-12	Random	PCBs not detected above laboratory reporting limits	1.12	593
PCB13-AIR-01-05	11/01/12	C-337	GROUND	At X-11	BEJ	PCBs not detected above laboratory reporting limits	1.12	589

* Limit of detection 0.01 µg/m³

3. COMPLIANCE MEASURES

3.1 PROCESS LUBRICATION OIL REMOVAL

Section 3.1 does not apply to Paducah Gaseous Diffusion Plant.

3.2 SPILL CLEANUP

3.2.1 Requirements

Attachment I, Section 2 (C), of the UE TSCA FFCA states the following:

Spill Cleanup – PCBs and PCB contaminated oil that may leak onto building floors shall be cleaned up in accordance with the EPA Spill Cleanup Policy. For spills >500 parts per million (ppm) PCBs, this shall consist of cleanup to 10 µg PCB/100 cm² with 95% confidence, based on the statistical sampling approach set forth in Attachment III, which shall be used within the spill area to verify cleanup to appropriate levels or, alternatively, to 100 µg PCB/100 cm² with 95% confidence, based on the statistical sampling approach set forth in Attachment III, which shall be used within the spill area to verify cleanup to appropriate levels followed by application of an appropriate sealant, such as a 2-layered epoxy type paint. All spill cleanups will be initiated within 24 hours of discovery, excluding historic spills which are defined as PCB stains resulting from spills which have occurred prior to the effective date of this Agreement. Historic spills may be left in place until demolition of the facility, provided public access to the facility is restricted to prevent unauthorized entry. In the event that a new spill should occur on a historic spill site, and the appropriate standard specified above cannot be met after best efforts to meet the standard are made, DOE may request that EPA consider the efforts DOE has made and classify the spill area as a historic spill for purposes of the cleanup under this Agreement.

3.2.2 Work Completion Date


None listed.

3.2.3 Activity for this Quarter

Twenty-three gasket spill sites were pending post-cleanup verification at the beginning of this reporting period. One gasket spill to the building floor was identified during the reporting period. Five gasket spill sites were closed during this reporting period by verifying sampling data. Nineteen gasket spill sites were pending post-cleanup verification at the end of this reporting period. PCB spill cleanup progress for CY 2012 is illustrated in Figure 1.

All PCB spills identified were high concentration PCB spills (i.e., from a source of 500 ppm or greater in PCB concentration). Cleanup of each identified spill site was initiated within 24 hours, in accordance with the UE TSCA FFCA. Clearly visible signs have been posted at each spill site advising personnel to avoid the area in order to minimize the spread of contamination and the potential for human exposure. The DOE remediation contractor maintains the cleanup documentation, and the records are available for inspection.

**PCB Gasket Spills
January 1 through December 31, 2012**

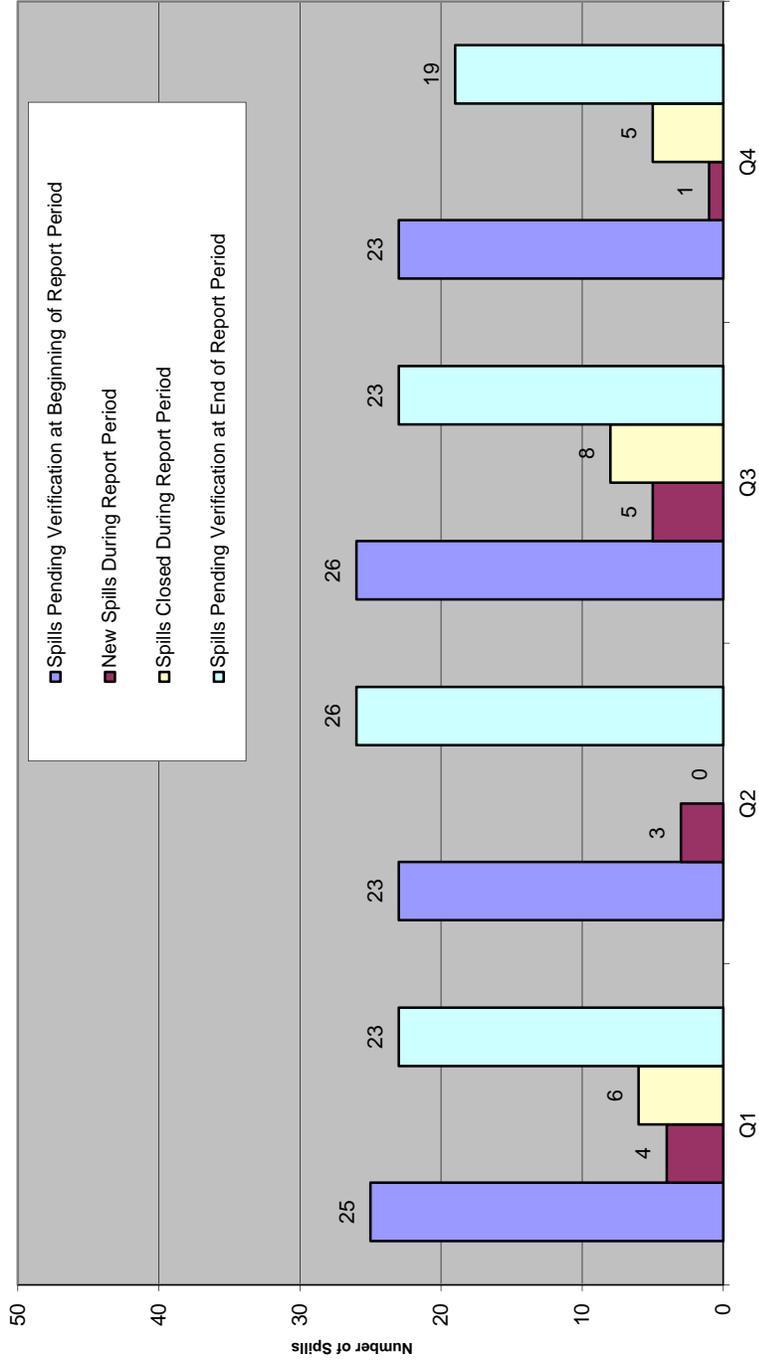

CY 2012

Note: All PCB Gasket spills are high concentration.

Figure 1. Quarterly Summary of PCB Gasket Spills

3.3 ELECTRICAL CABLES AND ASSOCIATED EQUIPMENT

3.3.1 Requirements

Attachment I, Section 2 (F), of the UE TSCA FFCA states the following:

Electrical Cables and Associated Equipment – PCB contaminated electrical cables and associated equipment shall be removed from the facilities upon decommissioning, unless they require maintenance, servicing or replacement during plant operations, or gasket removal. If maintained or serviced, the cables, cable trays, and associated equipment shall be removed or cleaned up to 10 µg PCB/100 cm² or 100 µg PCB/100 cm² with 95% confidence followed by application of appropriate sealant.

3.3.2 Work Completion Date

Work must be complete upon demolition.

3.3.3 Activity for this Quarter

During the fourth quarter of CY 2012, the C-340 Decontamination and Decommissioning project PCB remediation waste that was greater than 50 ppm PCB was packaged during demolition. The weight of this waste was 573,438 kg. The PCB bulk product waste (e.g., ventilation duct work, coated wires, and painted surfaces) were not segregated from the building demolition debris since the debris was managed as PCB remediation waste.

3.4 DISPOSAL

3.4.1 Requirements

Attachment I, Section 2 (G) of the UE TSCA FFCA states the following:

Disposal – All waste PCBs, PCB Items and ventilation ducts (and associated flanges), electrical cables and associated equipment contaminated with PCBs which were not decontaminated pursuant to Sections 2(C), 2(E), and 2(F) of this Attachment, shall be disposed of in accordance with 40 *CFR* § 761.60. All waste PCBs and PCB Items contaminated with hazardous waste and/or asbestos shall be disposed of in accordance with TSCA, NESHAP [National Emission Standard for Hazardous Air Pollutants] and RCRA [Resource Conservation and Recovery Act] requirements, and/or alternate disposal methods approved by EPA.

3.4.2 Work Completion Date

- Nonradioactive PCBs and PCB Items—within one year after the date the materials were placed into storage for disposal in accordance with Section 2(D) of the attachment of the UE TSCA FFCA.
- Co-contaminated, radioactive PCBs, and PCB items stored for disposal—within 10 years of work initiation date for materials already in storage; 2016, or within 10 years of storage, whichever date is earlier, for materials placed into storage after the effective date of the UE TSCA FFCA.

- Ventilation gaskets, ductwork and flanges, electrical cable, associated equipment, and historic spill material—2016, or within 10 years of work initiation date, whichever date is earlier.

3.4.3 Activity for this Quarter

During the fourth quarter CY 2012, 2,176 kg of PCB waste was shipped for disposal on one manifest and two Certificates of Disposal were received. The PCB waste disposal summary for this reporting period is shown in Table 2. Waste generated as a result of site cleanup and operations is included in this report, including Comprehensive Environmental Response, Compensation, and Liability Act waste, which is provided for information only and is intended to show progress toward removal of PCBs at Paducah.

**Table 2. PCB Waste Shipped Off-Site Disposal Activities:
Waste Shipped Off-Site and Certificates of Disposal Received
October 1 through December 31, 2012**

PCB Item Count	Description	Weight (kg)	Earliest Date Removed from Service	Date Shipped	Manifest	Shipment No.	Disposal Location	Disposal Method	Disposal Date	CD Rec'd No. of Items Disposed
1	ST-90 of PCB/LLW Debris	2,176	11/07/2011	11/16/2012	006841620JJK	6228-15-0019	EnergySolutions	Landfill		
2	PCB contaminated light fixtures from USEC originally in RFD 119355 and PCB contaminated capacitors from USEC light fixtures originally in RFD 119355	87	8/30/2011	7/31/2012	005669359FLE	005669359FLE	Clean Harbors Deer Park, TX	Incineration	10/05/2012 10/05/2012	10/15/2012 10/15/2012
1	Total Shipped	2,176								2
	Total Disposed	87								2

CD = Certificate of Disposal
 LLW = low-level waste
 PCB = polychlorinated biphenyl
 RFD = Request for Disposal
 USEC = United States Enrichment Corporation

All PCB waste listed is PCB/radioactive waste.
 Weights and volumes are taken from the Uniform Hazardous Waste Manifests.

Summary of Waste Disposal Activities for CY 2012 Fourth Quarter

Total Items Shipped for Treatment/Disposal: 1 Item (1 manifest)
Total Volume Shipped for Treatment/Disposal: 90 ft³
Total Weight Shipped for Treatment/Disposal: 2,176 kg
Total Items Disposed of per CDs Received: 2 Items (2 CDs: 87 kg; 3.14 ft³)
